

SOFTWARE ENGINEERING LAB 2

SRN -PES2UG24CS089


NAME – ARYAN MITTAL

EPICS AND USERSTORY AND STORYPOINTS

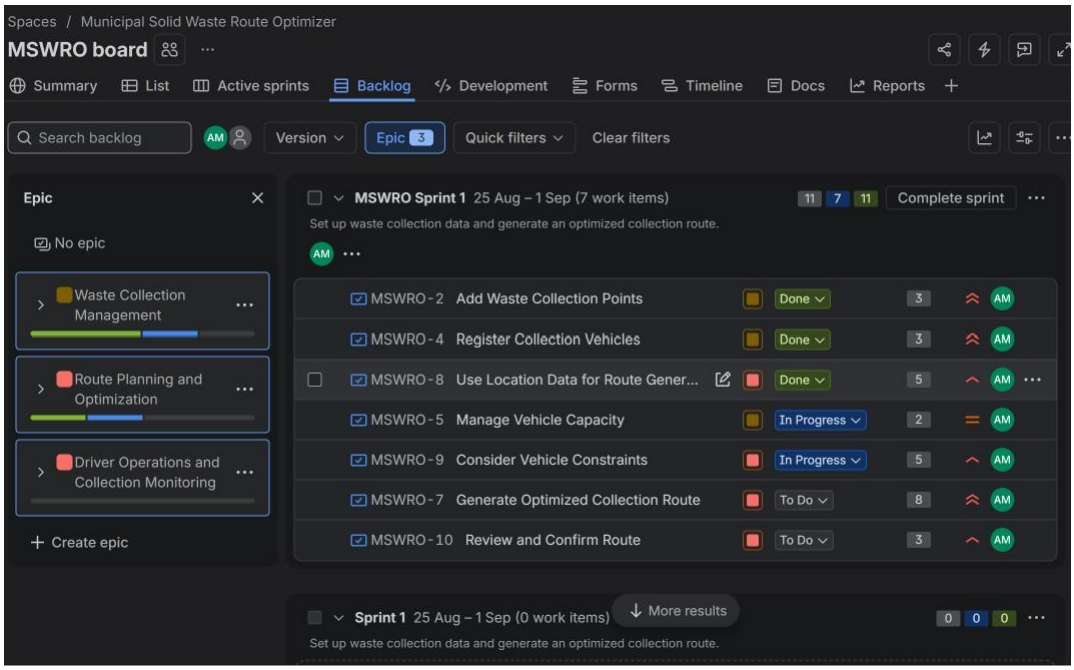

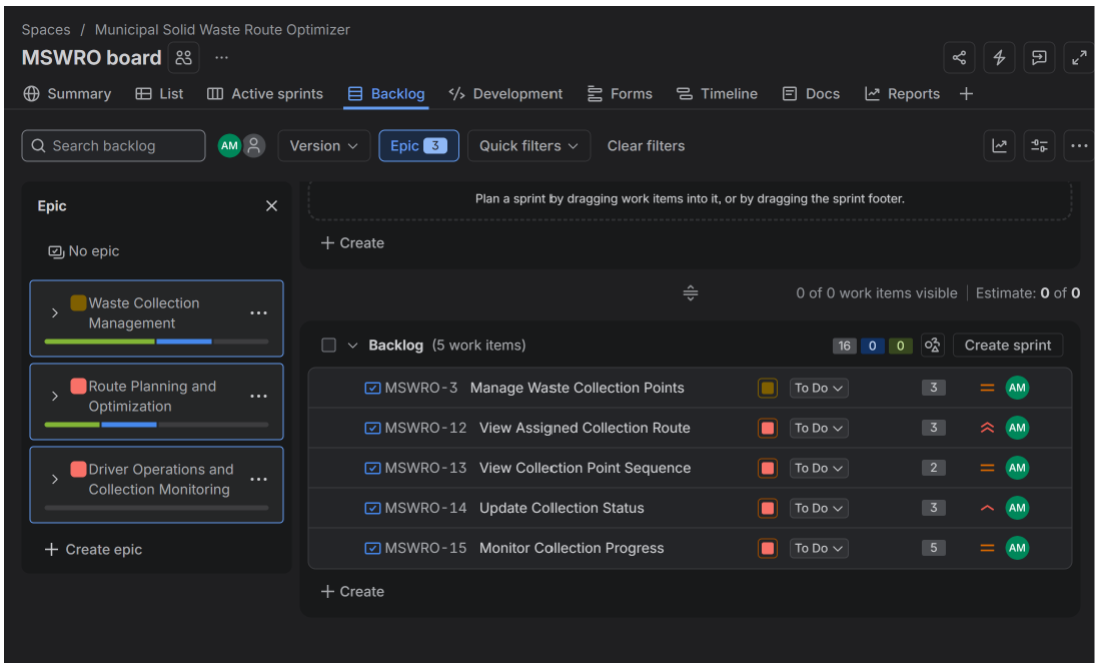


ACTIVE SPRINTS

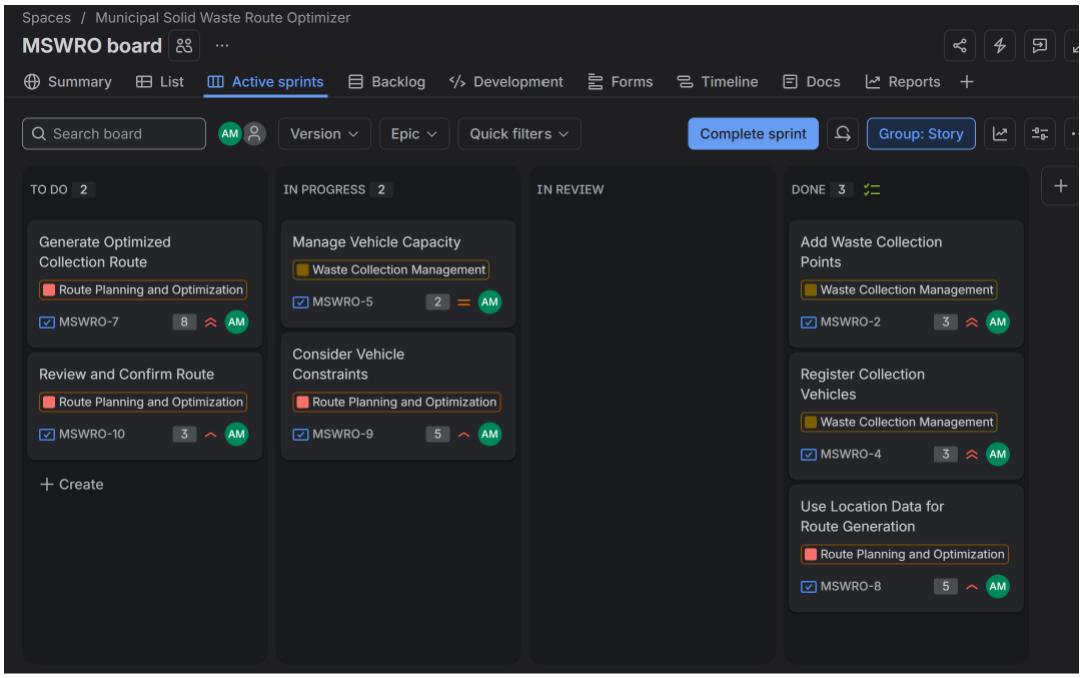

BURNDOWN CHART



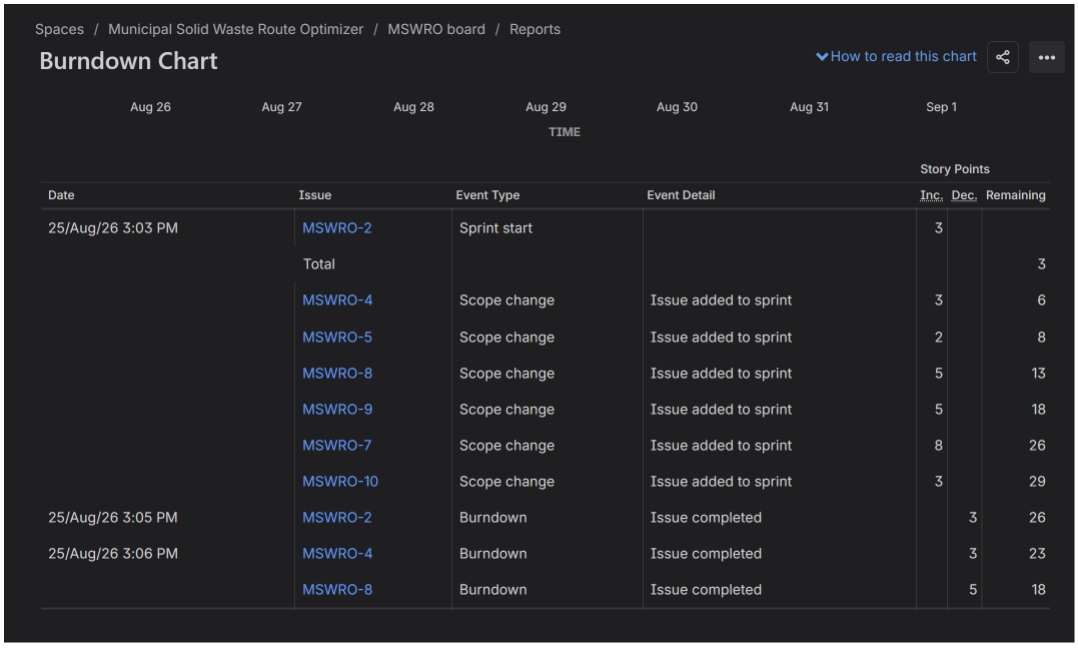

Spaces / Municipal Solid Waste Route Optimizer / MSWRO board / Reports

Burndown Chart

How to read this chart

Aug 26 Aug 27 Aug 28 Aug 29 Aug 30 Aug 31 Sep 1

TIME

Date	Issue	Event Type	Event Detail	Story Points Inc.	Dec.	Remaining
25/Aug/26 3:03 PM	MSWRO-2	Sprint start		3		
	Total					3
	MSWRO-4	Scope change	Issue added to sprint	3		6
	MSWRO-5	Scope change	Issue added to sprint	2		8
	MSWRO-8	Scope change	Issue added to sprint	5		13
	MSWRO-9	Scope change	Issue added to sprint	5		18
	MSWRO-7	Scope change	Issue added to sprint	8		26
	MSWRO-10	Scope change	Issue added to sprint	3		29
25/Aug/26 3:05 PM	MSWRO-2	Burndown	Issue completed		3	26
25/Aug/26 3:06 PM	MSWRO-4	Burndown	Issue completed		3	23
	MSWRO-8	Burndown	Issue completed		5	18

REFLECTION QS ANSWERS

Reflection Questions

1. Did your estimations reflect the actual effort?

The story point estimates provided a reasonable representation of the effort required for the user stories. Smaller tasks such as **Manage Vehicle Capacity** were assigned fewer points, while more complex tasks such as **Generate Optimized Collection Route** were assigned higher points. Since this was a simulated sprint, the estimates mainly helped us compare the relative complexity of the tasks.

2. Was your backlog well-prioritized?

Yes, the backlog was prioritized according to the importance and complexity of the work. Higher-priority stories related to **route planning and optimization** were given more attention, while supporting tasks such as vehicle and collection-point management were also included. This helped organize the work in a logical order.

3. How did your simulated sprint align with your plan?

The simulated sprint was aligned with the plan because the selected stories covered the main goals of setting up waste collection data and generating an optimized collection route. We planned **7 work items totaling 29 story points** for Sprint 1. During the sprint, some stories were completed, some were in progress, and the remaining stories stayed in the To Do column.

4. What insights did the burndown chart give about your team's capacity?

The Burndown Chart showed the amount of work remaining during the sprint and helped visualize the team's progress. The sprint started with **29 story points**, allowing

us to understand the planned workload and compare it with the work completed. It also showed that the team had limited capacity within the sprint and that completing all planned work would require steady progress throughout the sprint.
